




Monthly Photographs

KEY PLAN




THE RIGHT LIFE PROJECT

Phase 1.1 – Key Plan

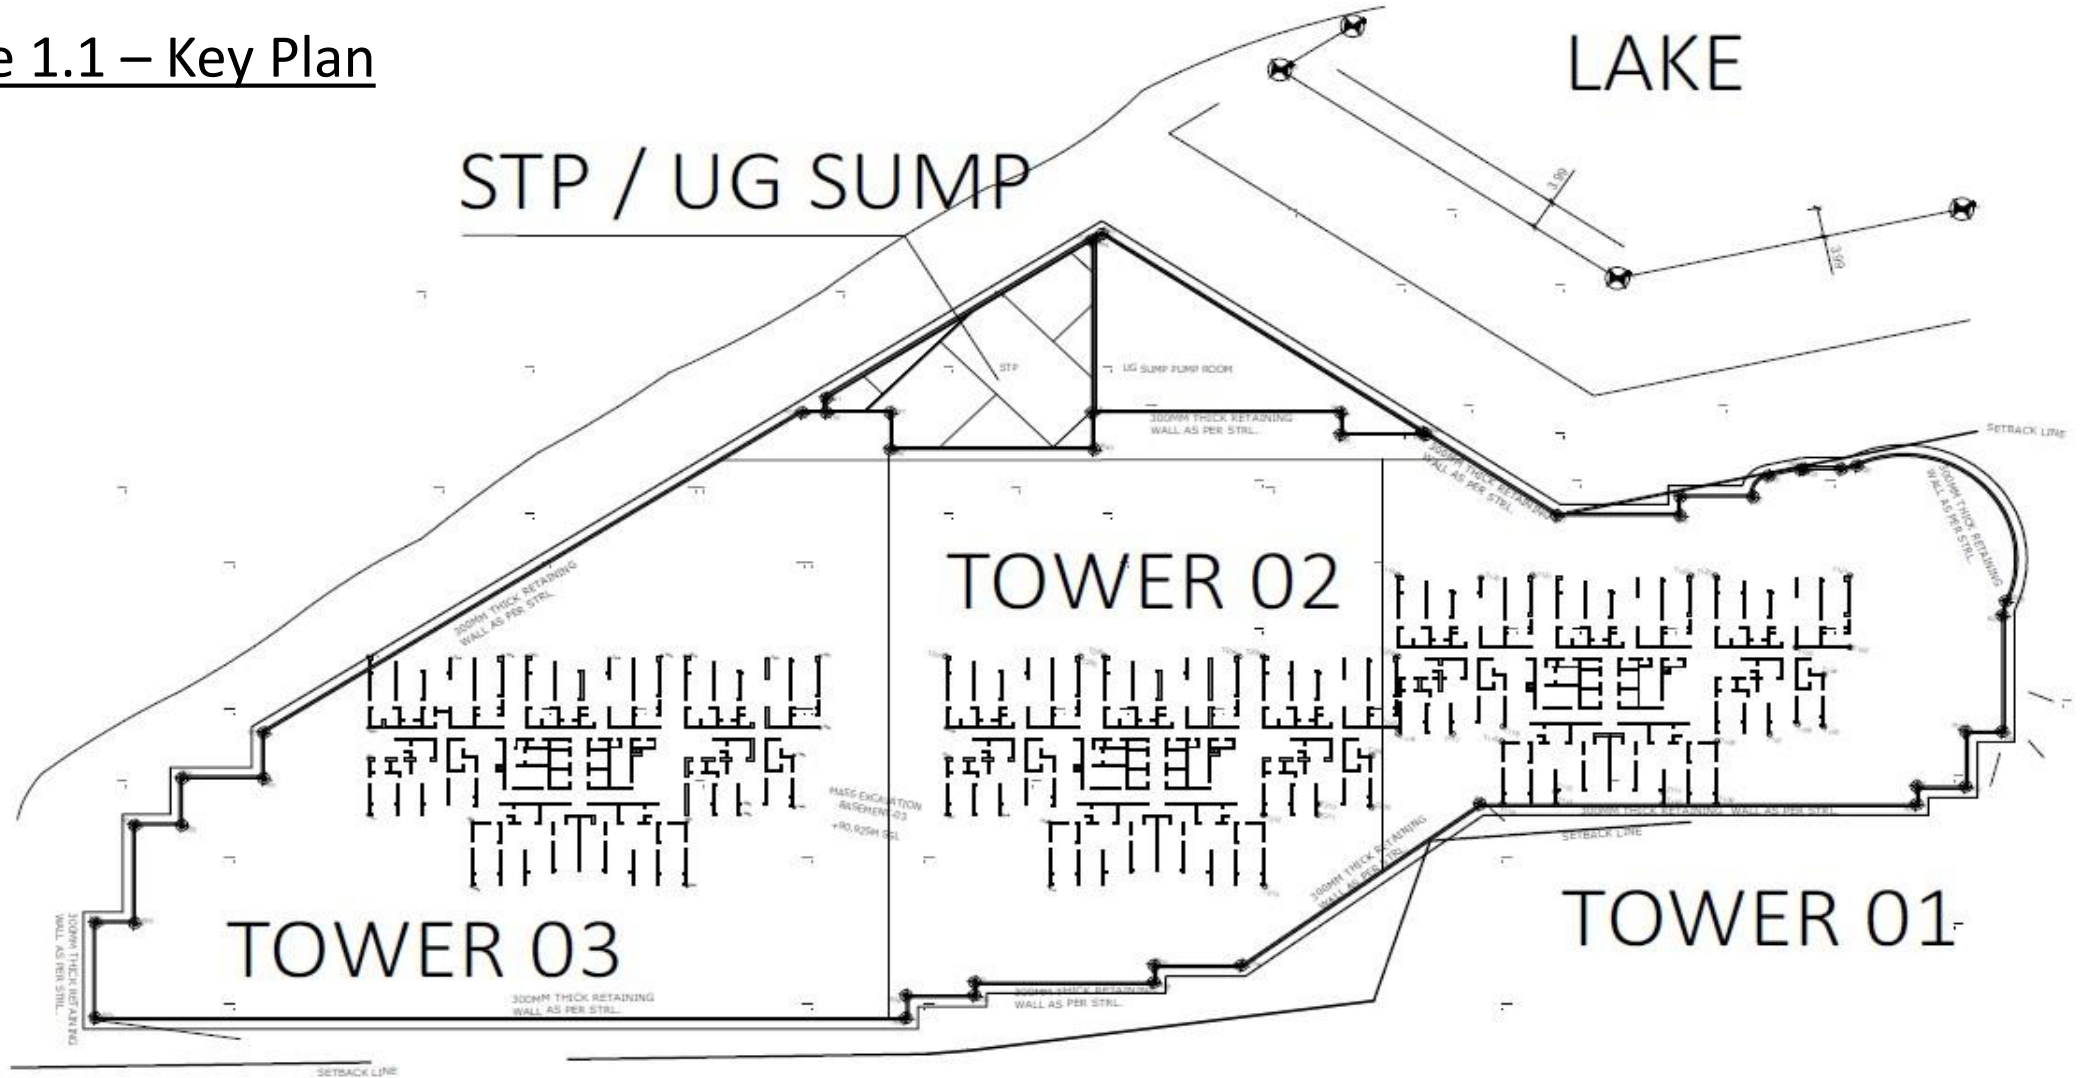

THE RIGHT LIFE PROJECT

Phase 1.1 – Tower 01



- B 03 Slab Pour 05 / 06 – Completed on 28-02-25.
- Basement 02 shear wall completed 63/73.
- B 02 Slab Pour 02 / 06 – Completed on 28-02-25.
- Basement 01 shear wall completed 18/73.

THE RIGHT LIFE PROJECT

Phase 1.1 – Tower 02



- B 03 Slab Pour 04 / 06 – Completed on 28-02-25.
- Basement 02 shear wall completed 72/72.
- B 02 Slab Pour 02 / 07 – Completed on 28-02-25.
- Basement 01 shear wall completed 12/72.

THE RIGHT LIFE PROJECT


Phase 1.1 – Tower 03



- PCC 7/8 Completed.
- Tower crane erection completed on 19-02-25
- Stitch slab 1/8 Completed.

THE RIGHT LIFE PROJECT

Phase 1.2 – Tower 07 - 09

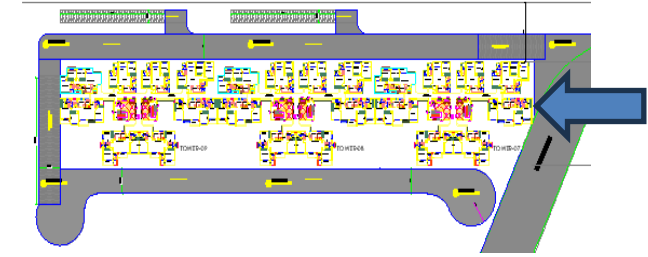

- Excavation 75% completed

THE RIGHT LIFE PROJECT

Achieved in the month of February

- Tower 01
 - Basement 03 Roof Slab Pour 03A – Concrete - Completed
 - Basement 03 Roof Slab Pour 05 – Concrete - Completed
 - Basement 02 Roof Slab Pour 01 – Concrete - Completed
 - Basement 02 Roof Slab Pour 02 – Concrete - Completed

- Tower 02
 - Basement 03 Roof Slab Pour 03A – Concrete - Completed
 - Basement 02 Roof Slab Pour 01 – Concrete - Completed
 - Basement 02 Roof Slab Pour 02 – Concrete - Completed

- Tower 03
 - Raft PCC Works - 80%
 - Stitch slab - 15%

THE RIGHT LIFE PROJECT

Target for the month of March

- Tower 01
 - Basement 03 Roof Slab Concrete - 100%
 - Basement 02 Roof Slab Concrete - 65%
 - Basement 01 Roof Slab Concrete - 15%

- Tower 02
 - Basement 03 Roof Slab Concrete - 100%
 - Basement 02 Roof Slab Concrete - 50%

- Tower 03
 - Raft PCC Works - 100%
 - Stitch slab - 50%
